GymPassJUST

Part 1: Initiation and Planning | SE440 CSP11 | Jordan University of Science and Technology

Report revision: 2 November 2026. System version: 1.2.2. Part 1 submission: 21 November 2026.

A concise PMP using the supplied MiniBook structure. Sections 0-16 contain the plan; sections 17-20 are short outlines. This is a team-review draft, not evidence of final course approval.

Member	Proposed responsibility
M1 Asia Bassam Ahmad Quraia	Planning, requirements and costs
M2 Mai Qaseem Mohammad Al Rabayah	Arabic/English interface and usability
M3 Alaa Al Din Ziad Ali Al Tawalbeh	Server, database and booking rules
M4 Oday Mahmoud Mohammad Al Hajj	Tests, deployment and support

M1-M4 identify planned owners throughout this report. Add student IDs and confirm actual section authors and contributions before submission. These assignments do not claim work performed by a student.

0 Project charter and business case (planned: M1)

The sports center needs one place to manage gym subscriptions, fair class bookings and attendance. A student buys a plan, books a class and shows a QR to the assigned instructor. The proposed sponsor is the Sports Center Director; the TA reviews the course deliverable. Neither sponsor acceptance nor university integration is claimed.

Success means no overbooking, FIFO promotion, valid class attendance checks and a clear bilingual interface. A proposed five-person usability test targets booking in at most three screens and under 30 seconds. This test is still pending.

The estimated baseline is JOD 2,240 (section 7). Assume annual benefits of JOD 1,800 less JOD 800 maintenance: net JOD 1,000. At 8% for three years, NPV = -2240 + 1000/1.08 + 1000/1.08² + 1000/1.08³ = **JOD 337.10**. These are planning assumptions, not actual savings.

1 Project overview (planned: M1)

Deliverables: working website and database; source and tests; Part 1 and final PDFs; user/run guides; diagrams and evidence. The first launch has four local accounts and three plans, with zero subscriptions or classes. Payments are simulated. Accounts are separate from official university accounts.

PMP = project management plan; FIFO = first in, first out; QR = signed rotating student pass; API = browser/server interface; NPV = today's value of future benefits. Source: github.com/3latw/GymPassJUST. References and AI disclosure appear on page 10.

2 Life cycle (planned: M1)

Use three short sprints: accounts/plans, booking/waitlist, then QR/reports. Demonstrate each slice and test its rules before the next one. Small increments suit four members and allow TA feedback. Update this plan through the change process in section 3.

3 Organization and governance (planned: M1)

Hold a weekly 20-minute meeting and record tasks, decisions and blockers. The feature owner implements; a different member reviews. M1 records changes; all affected owners estimate effort; the TA/sponsor decides material scope, cost or date changes. Do not promise an unapproved feature.

Work / RACI	M1	M2	M3	M4
Plan and requirements	A/R	C	C	C
Interface	A	R	C	C
Database and rules	A	C	R	C
Verification and handover	A	C	C	R

R does the task, A is accountable, C is consulted. Notify the TA at each milestone (I). Working agreement: small real commits, no shared passwords in Git, peer review, and early notice of missed work. Record actual contributions rather than creating a fake history.

4 Scope, requirements and acceptance (planned: M1 + M3)

ID / requirement	Simple acceptance check	Trace
FR01-02: accounts and plans	Public signup creates only a student; only manager edits plans.	accounts / HTTP
FR03: simulated subscription	Reject the same active/queued plan; identical payment retry is safe.	current scope
FR04: publish classes	Instructor publishes own class; reject invalid time/capacity or room clash.	rules / HTTP
FR05: booking	Within 48h, require a suitable active plan; reject duplicate and overlap; no overflow.	rules / load
FR06-07: FIFO and cancellation	Student cancels at least 2h before start; first eligible waiter gets the place.	rules
FR08-09,15: QR attendance	Assigned instructor scans a valid pass during class; require BOTH plan and confirmed booking.	current scope / decoder
FR10,14: attendance history	At class end, scanned becomes attended; unscanned confirmed becomes no_show.	current scope
FR11-12: notifications / class cancellation	No duplicate notice. Assigned instructor or manager can cancel until class end.	current scope / HTTP
FR13,16: reports / audit	Manager totals come from saved records; students see only their own history.	HTTP / current scope

Test names above refer to tests/accounts.test.js, http.test.js, rules.test.js, current-scope.test.js and qr-decoder.test.js. Full mapping: docs/requirements-traceability.md. The cancellation boundary and QR conditions are release acceptance rules.

WBS: 1 planning (requirements, cost, risks); 2 design (data, API, pages); 3 implementation (accounts, plans, booking, QR); 4 verification (rules, load, usability); 5 handover (backup, guides, acceptance). Each item has a named owner and a reviewable output.

Scope limits: no reception/security account, manual attendance, automatic seven-day suspension, real payment gateway or deployed university SSO. Cancelled/completed classes leave the timetable after 24 hours; history stays stored. A request outside scope needs an impact estimate and a recorded decision.

Nonfunctional requirements: enforce roles on the server; retain data on restart; Arabic RTL and English LTR; keyboard-operable pages at 360px; backend statement coverage at least 70%; no overflow at 100 concurrent bookings; p95 below 2s at 300. See sections 11-12 and 16 for evidence and pending checks.

5 Architecture and design (planned: M2 + M3)

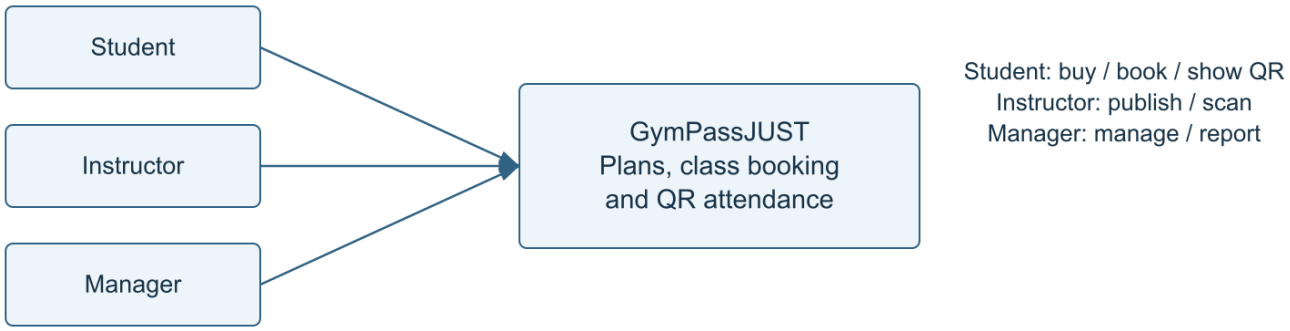


Figure 1. C4 context: the three users and their main jobs.




Figure 2. C4 containers: a browser, one Node service and one SQLite database.





Figure 3. Deployment: verified local Node setup; Docker is an optional packaging path, not a claimed hosted deployment.

Decision	Reason and trade-off
HTML/CSS/plain JavaScript	Simple pages that the team can read; no frontend framework is needed.
Node.js 24 + Express 5	JavaScript on both sides; the server controls permissions and business rules.
SQLite + transactions + capacity trigger	Easy local setup and persistent storage; intended for one application instance.
Signed short-lived QR + server recheck	The QR identifies the student; live plan and booking checks decide attendance.

Trust boundary: browser input is untrusted. Requests pass through authentication, CSRF and role checks before the service reads or changes data. Local HTTP is for demonstration; hosted camera access requires HTTPS.

5 continued: data and interfaces

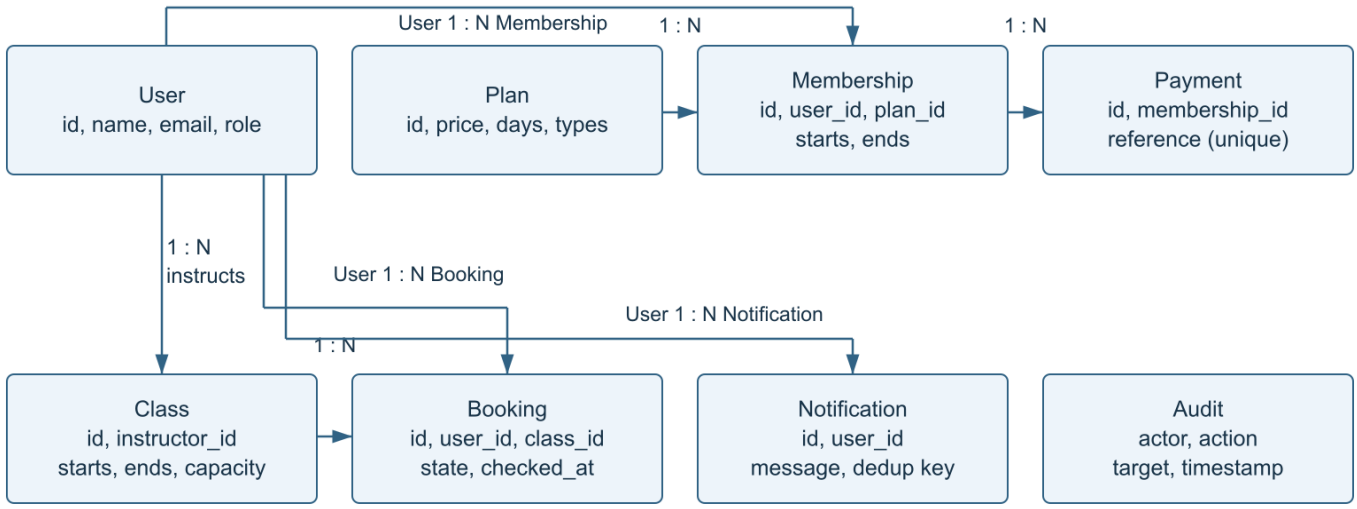

Credential is 1:1 with User; sessions are 1:N. Audit actor is recorded text, not a foreign key.

Figure 4. Core entity relationships. Arrows point from one record to its many related records. Technical and legacy tables are omitted for clarity.

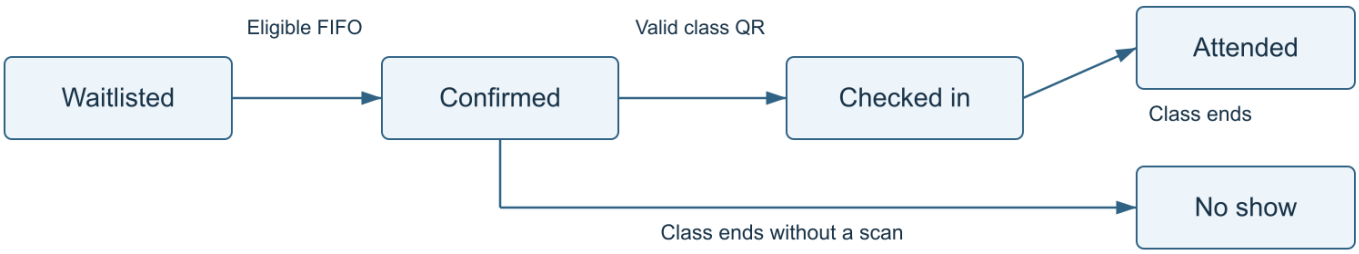


Figure 5. Main booking states. Students may also cancel before the cutoff; class cancellation closes remaining bookings. An unpromoted waitlist closes when the class ends.

Main REST path (base /api)	Purpose / access
POST /auth/local/register, /auth/local/login	Create a student account or authenticate with email/password.
GET/POST /plans; POST /memberships	View plans; manager creates plans; student buys with Idempotency-Key.
GET/POST /classes; POST /classes/:id/cancellation	List/publish classes; assigned instructor or manager cancels.
POST /bookings; GET /bookings	Book a class; read own history.
POST /bookings/:id/cancellation	Student cancels own booking before the cutoff.
GET /membership-pass; POST /class-qr-check-ins	Student receives QR; instructor validates and records attendance.
GET /classes/:id/roster; GET /dashboard, /audit	Authorized roster; manager aggregates and audit.

Full contract: docs/API.md. Auth routes are /auth/local/* (outside /api). Other listed paths use /api. JSON times are Unix milliseconds. Protected requests use session cookies; mutations require the correct Origin and CSRF token. Typical errors: 401 login, 403 access, 404 missing, 409 conflict, 422 invalid input, 429 limit.

5 continued: interaction sequences

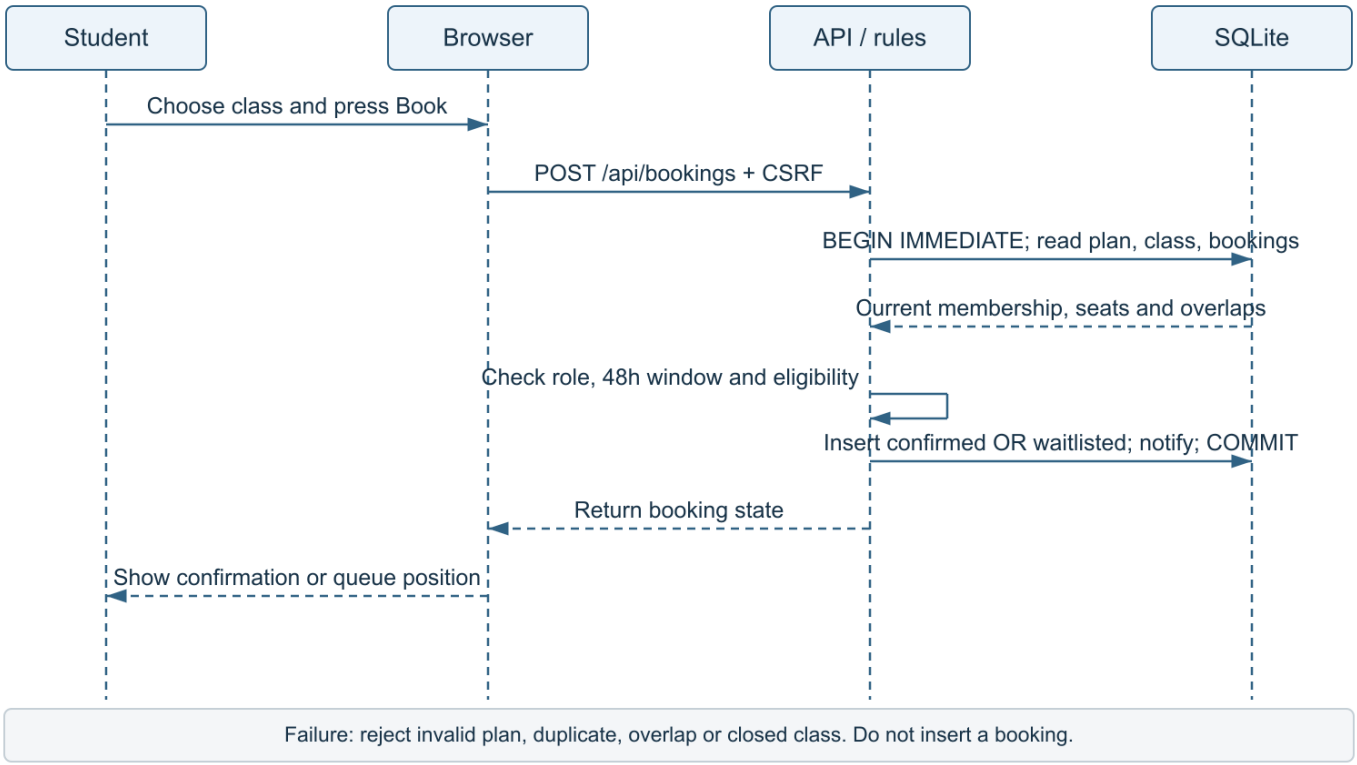


Figure 6. Booking sequence: validate eligibility and allocate a seat or waitlist place in one transaction.

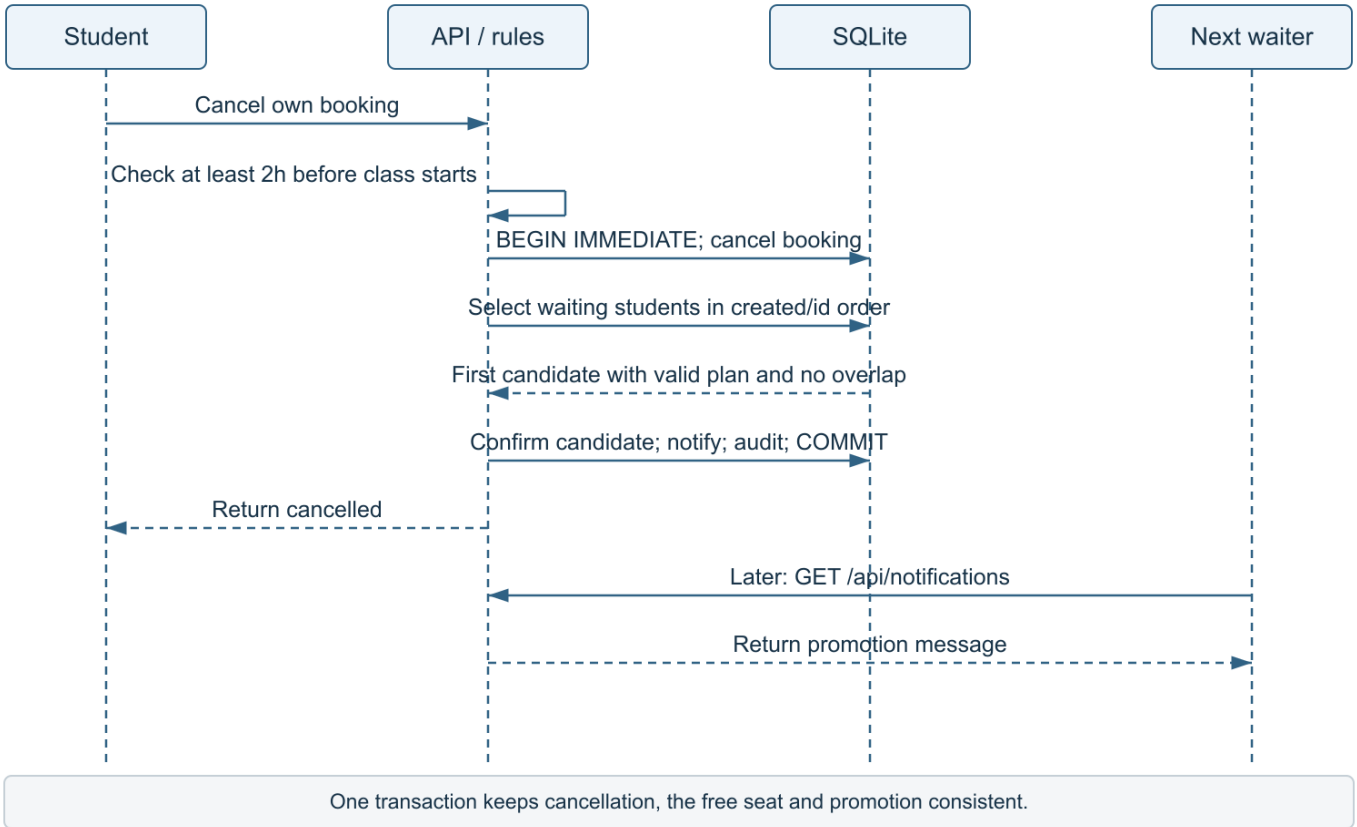


Figure 7. Cancellation/FIFO sequence: the first eligible waiting student receives the freed seat.

These lifeline diagrams show the successful paths. Rejected checks return an error without a partial update. The template's room/lab approval interaction is replaced by the gym's cancellation/FIFO interaction because this project does not have lab approvals.

5 continued: QR and screen design

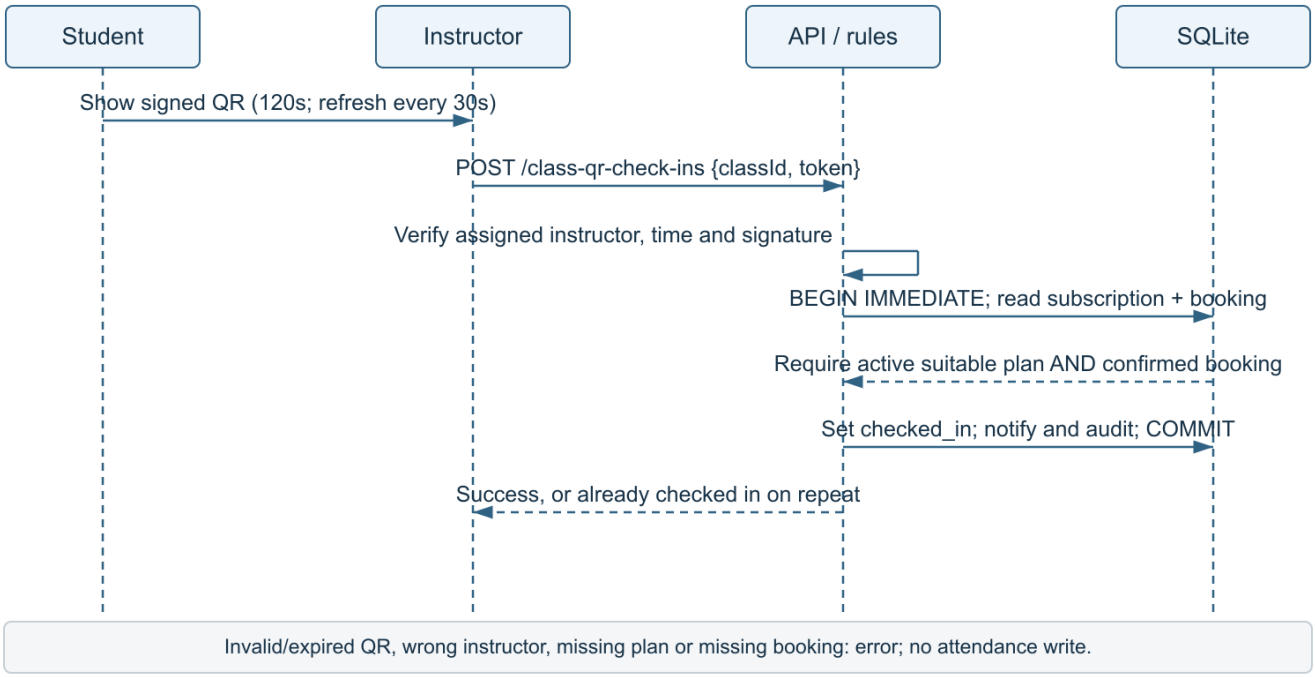


Figure 8. Instructor QR sequence. Scanning is allowed from class start until just before class end, with no ten-minute limit.

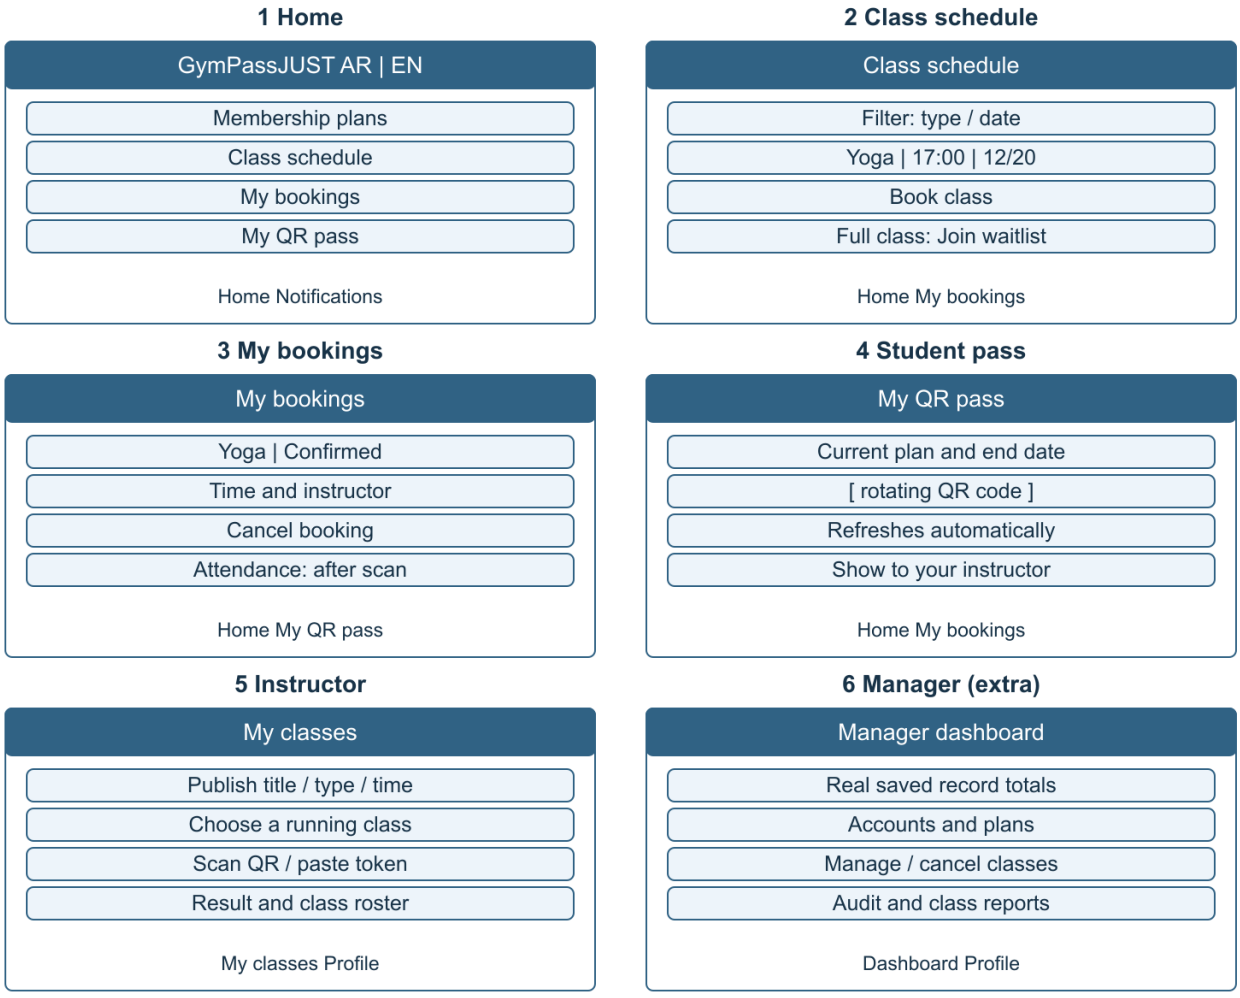


Figure 9. Five required low-fidelity screens plus an extra manager screen. Labels are English for the report; the implemented interface switches Arabic/English.

The student pass lasts 120 seconds from issue and refreshes every 30 seconds. A valid repeated scan returns already checked in. At class end, the minute job finalizes attendance; absence time is the original class end even after downtime.

6 Schedule and estimates (planned: M1)

Period / milestone	Output and dependency	Hours
Weeks 1-2: initiation	Charter, scope and risks before design	48
Weeks 3-4: design	Data, API and wireframes before construction	64
Weeks 5-7: accounts / plans	Sprint 1; Part 1 report due 21 Nov 2026	80
Weeks 8-10: booking / FIFO	Sprint 2; depends on users and plans	88
Weeks 11-12: QR / tests	Sprint 3; depends on confirmed bookings	72
Weeks 13-14: handover	Pilot, documentation, final report due 9 Jan 2027	32

Total planned work: 384h; reserve: 64h. These are course-week estimates, not a claim that the full timetable has elapsed. Part 1 discussion: 22-28 Nov; final discussion: 10-16 Jan; week-15 test date is pending. Estimates use small task breakdowns and weekly actual/remaining-hour review.

Critical path: approved scope → data/API design → accounts/plans → booking/FIFO → QR → verification → handover. UI can run in parallel after the API draft. Keep the reserve for identified risks; escalate a forecast date slip or more than 10% effort variance.

7 Cost and effort baseline (planned: M1)

Item	Calculation	JOD
Planned work	384h × 5 JOD/h	1,920
Risk contingency	64h × 5 JOD/h	320
Cost baseline (BAC)	448h × 5 JOD/h	2,240
Management reserve	10% of baseline; sponsor controlled	224
Total funding ceiling	Baseline + management reserve	2,464

Each member has 8h/week for 14 weeks: 112h each, 448h total. Free/local tools are assumed; any paid hosting or new procurement needs approval. Track actual hours weekly. Credit completed tasks only after review/tests; multiply hours by the assumed rate for EVM.

EVM teaching example, not measured team spending: PV=800, EV=720, AC=900. SV=EV-PV=-80; CV=EV-AC=-180; SPI=.90; CPI=.80. With BAC=2240, EAC=BAC/CPI=2800; ETC=1900; VAC=-560. Replace the example with real earned-value data when available.

8 Resources and team development (planned: M1)

M1 leads planning; M2 owns the interface; M3 owns rules/data; M4 owns verification and handover. Each has 96 planned hours plus 16 reserve hours. Pair M2/M3 on API integration and M3/M4 on race and QR tests. Onboarding: run the README, use isolated test accounts, read the Arabic code guide and demonstrate one reviewed change. Rotate reviewers and rehearse all three account roles.

9 Stakeholders and communication (planned: M1)

Stakeholder / power-interest	Communication and engagement
TA / proposed sponsor: high-high	Weekly short status and milestone demo; request scope/acceptance decisions.
Instructor / manager: medium-high	Review publishing, roster and QR flow at sprint demos.
Students: low-high	Recruit five volunteers for booking and QR usability tasks; collect coded feedback.
University IT: high-medium	Consult before hosting, real identity integration or a policy decision.

10 Risk plan (planned: M1 + M4)

Estimate probability 0-1 and lost effort hours; prioritize probability × impact. Review weekly and when a trigger occurs. The groups below retain every ID in the detailed risk register. Expected exposure is 60.4h; reserve is 64h.

Risk IDs / owner / exposure	Trigger and response
R01,14 / M1 / 10.4h	Capacity or course interpretation changes: protect Must scope and seek TA decision.
R02,04,05 / M3,M4 / 12h	Overflow, FIFO or end-time test fails: transaction/clock tests and immediate repair.
R03,06,10 / M1,M3 / 12.8h	Login/QR/security failure: deny invalid access, protect keys, review permissions.
R07,12 / M2 / 9.6h	RTL overflow or UI/API mismatch: device, keyboard and integration checks.
R08,09,11 / M4 / 12h	Hosting, restore or volunteer delay: local demo, restore drill, recruit early.
R13 / M4 / 3.6h	Audit/version alert: inspect advisory and test isolated upgrades.

11 Quality management (planned: M4)

Definition of Done: acceptance rule demonstrated, relevant tests pass, peer review complete, API/docs current, and no known blocking defect. Targets: ≥70% backend statement coverage, zero overbooking, p95 <2s at 300 concurrent bookings, no role bypass, readable Arabic/English at 360px. M4 records evidence; the owner fixes defects. Usability, full device/accessibility checks and independent acceptance remain pending.

12 Security and privacy (planned: M3 + M4)

Threat	Control and verification
Impersonation / account guessing	Salted scrypt hashes, request limits and server sessions; account/HTTP tests.
Role bypass / forged request	Server-side role/ownership checks, Origin + CSRF, prepared SQL and escaped text.
Forged, expired or reused QR	Signature/purpose/expiry plus live plan/booking checks; duplicate scan is safe, not a second attendance event.
Private data or database loss	Own-record access, protected files, backup/restore and no credentials/database in public Git.

Collect only needed account and booking data. Use synthetic data for tests and coded usability notes. Proposed retention and deletion rules need university approval; do not invent a legal retention period. Hosted HTTPS and a security review are required before real deployment.

13 Procurement and tooling (planned: M4)

Build the gym rules; reuse maintained infrastructure. Node/Express, qrcode, jsQR and jose use MIT licenses; c8 uses ISC and SQLite is public domain. Check installed LICENSE files before redistribution. Use GitHub for source; Docker is optional. No paid service is purchased. Keep attribution, the lockfile and the upstream license files; avoid adding a payment/identity service without approval.

14 Configuration and release management (planned: M3 + M4)

Configuration items: source, schema/migrations, lockfile, tests, report/diagram sources, guides and evidence. Use short branches and reviewed real commits; tag a release only after checks. Baseline: v1.2.2 with dated evidence. Keep .env, accounts, signing keys, live data and backups out of public Git. A report-only revision does not change the application version. Retain the last working package and a database backup for rollback.

15 Construction and integration (planned: M2 + M3)

Implement accounts/plans, then booking/FIFO, then QR/manager reports. Use descriptive JavaScript names and small functions. Keep validation and state changes in the service rather than trusting the page. Review each change, run syntax/unit/HTTP checks, and integrate a passing slice. The proposed CI quality gate is the same checked-in test/coverage command; do not claim a hosted pipeline run without its record.

16 Verification and validation (planned: M4)

Use isolated databases and an injected clock. Test boundaries, invalid inputs, equivalence groups and concurrent requests. Levels: rule/unit, database/API integration, browser role flows and planned user acceptance. Entry: install works, contract is stable and fixtures are separate. Exit: all automated tests pass, no blocking defects and acceptance evidence is reviewed.

Check / source	Observed local result on 2 Nov 2026
Automated suite / evidence/test-results.txt	30 passed. Backend statements 93.92%; branches 86.32%.
Capacity / evidence/load-results.json	100 requests: 20 confirmed + 80 waiting; zero errors; p95 527.36ms.
Capacity / same file	300 requests: 20 confirmed + 280 waiting; zero errors; p95 894.84ms.
Fresh package / fresh-package-smoke.json	Four initial logins; database integrity OK; saved credentials survive restart.
Browser / simple-browser-checks.json	Student booking, language switch, instructor QR and class cancellation checked.

Load setup: Windows, Node 24.14.1, i7-8650U, one process, disk SQLite/WAL, loopback HTTP, pre-created sessions, no WAN/TLS/proxy. Results are not a hosted capacity promise. QR failure tests include missing plan, missing booking, wrong instructor, invalid/expired token and repeat scan.

Hardware camera scanning, five-person usability, full browser/WCAG checks and independent security acceptance are pending. Log each defect with steps, expected/actual result, severity and owner; fix blockers, rerun the relevant checks and retain evidence. Do not fill in participant results that did not happen.

17 Deployment and transition (outline) (planned: M4)

Plan a local Node demonstration first; keep Docker optional. Before pilot use, rehearse install, migration, backup/restore, role checks and rollback with a copied database. Confirm HTTPS/camera and sponsor approval. Full steps are reserved for the final report and README.

18 Operations and support (outline) (planned: M4)

Plan support hours, an incident contact, response targets and user training before pilot. Monitor startup, scheduler errors, failed backups, access errors and disk space. Keep minimal logs without passwords or QR tokens. Use README, the code guide and a three-role demonstration for handover.

19 Maintenance (outline) (planned: M3 + M4)

Proposed yearly effort: 48h corrective + 40h adaptive + 32h preventive + 40h improvements = 160h, or JOD 800 at the assumed rate. Review issues/dependencies monthly; prioritize a security or data-integrity fix immediately, then test before release. Keep technical debt and feature requests in the backlog. This is an estimate, not a support contract.

20 Monitoring, control and closure (outline) (planned: M1)

Track completed/remaining hours, milestones, risks and issues weekly. Use the section-7 EVM example only for explanation until real figures exist. Change record: manual/reception attendance replaced by instructor QR; duplicate-plan purchase blocked; class cancellation and 24h timetable hiding added. These match the current scope.

For closure, collect real acceptance evidence, actual author/contribution records and lessons learned; hand over source, accounts securely, guides and backups. Track the pending user/device/security checks and obtain TA acceptance.

Appendix A: AI assistance disclosure

Tool: OpenAI Codex. Purpose: coding/refactoring help, draft documentation, diagrams and automated checks. Changes in this revision: shorter English, ten-page layout, gym-specific sequences and wireframes, corrected QR/cancellation wording and dated evidence. Students must review, run, understand and correct the work and record their actual contributions. AI use is disclosed as required by the supplied template.

References and use of the template

[1] Supplied TemplateCSP_MiniBook.pdf: PDF pages 8-12 (PMP 0-20, deliverables, authors and AI), page 20 (design figures). [2] Supplied SE440 submission-schedule screenshot: 21 Nov 2026 and 9 Jan 2027. [3] Supplied CSP11 project brief and the user's later gym rules. [4] Project README, docs/API.md, requirements-traceability.md and evidence/. The template's UniRoom rooms/labs are examples; this report applies its structure to GymPassJUST.
